Kambala Estate

ID	Task Name	Duration	Start	Finish
1	**Kambala Estate**	**181 days**	**Fri 26/12/25**	**Fri 04/09/26**
2	Receipt of Order	1 day	Fri 26/12/25	Fri 26/12/25
3	**Mobilisation Period**	**30 days**	**Mon 29/12/25**	**Fri 06/02/26**
4	Place Orders with Supply chain	6 wks	Mon 29/12/25	Fri 06/02/26
5	Submit application to Building Contr	1 wk	Mon 29/12/25	Fri 02/01/26
6	**Construction Phase**	**150 days**	**Mon 09/02/26**	**Fri 04/09/26**
7	Site Set up	5 days	Mon 09/02/26	Fri 13/02/26
8	**1-6 Hicks Close**	**26 days**	**Mon 16/02/26**	**Mon 23/03/26**
9	Scaffold Erection	2 days	Mon 16/02/26	Tue 17/02/26
10	Asbestos Survey	1 day	Wed 18/02/26	Wed 18/02/26
11	Clean masonry and roof coverings	2 days	Wed 18/02/26	Thu 19/02/26
12	Clean through gutters & down pip	1 day	Fri 20/02/26	Fri 20/02/26
13	Roof Inspection & Report	1 day	Mon 23/02/26	Mon 23/02/26
14	Roof repairs	2 days	Tue 24/02/26	Wed 25/02/26
15	Liquid Waterproof coating to to rear terrace area	2 days	Wed 18/02/26	Thu 19/02/26
16	Clean & Overhaul windows	3 days	Fri 20/02/26	Tue 24/02/26
17	Masonry Repairs	5 days	Fri 20/02/26	Thu 26/02/26
18	Timber repairs generally to fascias / soffits / gates / bin	5 days	Mon 23/02/26	Fri 27/02/26
19	External Decorations	5 days	Mon 02/03/26	Fri 06/03/26
20	Internal Decorations	3 days	Fri 06/03/26	Tue 10/03/26
21	Survey flat FED's & report	1 day	Mon 16/02/26	Mon 16/02/26
22	Overhaul communal & FED doors	3 days	Tue 03/03/26	Thu 05/03/26
23	Contar Resin coatings to commun	3 days	Wed 11/03/26	Fri 13/03/26
24	Overhaul / replace electric fans	2 days	Fri 20/02/26	Mon 23/02/26
25	FRA works	3 days	Thu 05/03/26	Mon 09/03/26
26	CCTV to drainage	1 day	Mon 23/03/26	Mon 23/03/26
27	Scaffold Strike	1 day	Mon 09/03/26	Mon 09/03/26
28	**7-11 Hicks Close**	**26 days**	**Tue 17/02/26**	**Tue 24/03/26**
29	Scaffold Erection	2 days	Wed 18/02/26	Thu 19/02/26
30	Asbestos Survey	1 day	Fri 20/02/26	Fri 20/02/26
31	Clean masonry	2 days	Fri 20/02/26	Mon 23/02/26
32	Clean through gutters & down pip	1 day	Tue 24/02/26	Tue 24/02/26
33	Roof Inspection & Report	1 day	Fri 20/02/26	Fri 20/02/26
34	Roof repairs	2 days	Mon 23/02/26	Tue 24/02/26
35	Liquid Waterproof coating to to rear terrace area	2 days	Fri 20/02/26	Mon 23/02/26
36	Clean & Overhaul windows	3 days	Wed 25/02/26	Fri 27/02/26
37	Masonry Repairs	5 days	Wed 25/02/26	Tue 03/03/26
38	Timber repairs generally to fascias / soffits / gates / bin	5 days	Mon 02/03/26	Fri 06/03/26
39	External Decorations	5 days	Mon 09/03/26	Fri 13/03/26
40	Survey flat FED's & report	1 day	Tue 17/02/26	Tue 17/02/26
41	Overhaul communal & FED doors	3 days	Fri 06/03/26	Tue 10/03/26
42	Overhaul / replace electric fans	2 days	Tue 24/02/26	Wed 25/02/26
43	CCTV to drainage	1 day	Tue 24/03/26	Tue 24/03/26
44	Scaffold Strike	1 day	Mon 16/03/26	Mon 16/03/26
45	**12-29 Hicks Close**	**38 days**	**Wed 18/02/26**	**Fri 10/04/26**
46	Scaffold Erection	5 days	Mon 02/03/26	Fri 06/03/26
47	Asbestos Survey	1 day	Mon 09/03/26	Mon 09/03/26
48	Clean masonry	1 day	Mon 09/03/26	Mon 09/03/26
49	Clean through gutters & down pip	1 day	Tue 10/03/26	Tue 10/03/26
50	Roof Inspection & Report	1 day	Wed 11/03/26	Wed 11/03/26
51	Roof repairs	4 days	Thu 12/03/26	Tue 17/03/26
52	Clean & Overhaul windows	6 days	Wed 11/03/26	Wed 18/03/26
53	Masonry Repairs	7 days	Wed 11/03/26	Thu 19/03/26
54	Timber repairs generally to fascias / soffits / gates / bin	7 days	Thu 19/03/26	Fri 27/03/26
55	External Decorations	7 days	Mon 30/03/26	Tue 07/04/26
56	Internal Decorations	5 days	Wed 18/03/26	Tue 24/03/26
57	Survey flat FED's & report	1 day	Wed 18/02/26	Wed 18/02/26
58	Overhaul communal & FED doors	5 days	Wed 11/03/26	Tue 17/03/26
59	Contar Resin coatings to commun	5 days	Wed 25/03/26	Tue 31/03/26
60	Overhaul / replace electric fans	4 days	Thu 26/02/26	Tue 03/03/26
61	FRA works	3 days	Tue 10/03/26	Thu 12/03/26
62	CCTV to drainage	1 day	Wed 25/03/26	Wed 25/03/26
63	Scaffold Strike	3 days	Wed 08/04/26	Fri 10/04/26
64	**2-36 Ingrave Street**	**43 days**	**Thu 19/02/26**	**Mon 20/04/26**
65	Scaffold Erection	6 days	Mon 09/03/26	Mon 16/03/26
66	Asbestos Survey	1 day	Tue 17/03/26	Tue 17/03/26
67	Clean masonry	1 day	Tue 17/03/26	Tue 17/03/26
68	Clean through gutters & down pip	1 day	Wed 18/03/26	Wed 18/03/26
69	Roof Inspection & Report	1 day	Thu 19/03/26	Thu 19/03/26
70	Roof repairs	4 days	Fri 20/03/26	Wed 25/03/26
71	Clean & Overhaul windows	6 days	Thu 19/03/26	Thu 26/03/26
72	Masonry Repairs	7 days	Thu 19/03/26	Fri 27/03/26
73	Timber repairs generally to fascias / soffits / gates / bin	7 days	Fri 27/03/26	Mon 06/04/26
74	External Decorations	7 days	Tue 07/04/26	Wed 15/04/26
75	Internal Decorations	5 days	Wed 25/03/26	Tue 31/03/26
76	Survey flat FED's & report	1 day	Thu 19/02/26	Thu 19/02/26
77	Overhaul communal & FED doors	5 days	Wed 18/03/26	Tue 24/03/26
78	Contar Resin coatings to commun	5 days	Wed 01/04/26	Tue 07/04/26
79	Overhaul / replace electric fans	4 days	Wed 04/03/26	Mon 09/03/26
80	FRA works	3 days	Fri 13/03/26	Tue 17/03/26
81	CCTV to drainage	1 day	Thu 26/03/26	Thu 26/03/26
82	Scaffold Strike	3 days	Thu 16/04/26	Mon 20/04/26
83	**38-54 Ingrave Street**	**40 days**	**Fri 20/02/26**	**Thu 16/04/26**
84	Scaffold Erection	4 days	Tue 17/03/26	Fri 20/03/26
85	Asbestos Survey	1 day	Mon 23/03/26	Mon 23/03/26
86	Clean masonry	1 day	Mon 23/03/26	Mon 23/03/26
87	Clean through gutters & down pip	1 day	Tue 24/03/26	Tue 24/03/26
88	Roof Inspection & Report	1 day	Wed 25/03/26	Wed 25/03/26
89	Roof repairs	3 days	Thu 26/03/26	Mon 30/03/26
90	Clean & Overhaul windows	5 days	Wed 25/03/26	Tue 31/03/26
91	Masonry Repairs	5 days	Wed 25/03/26	Tue 31/03/26
92	Timber repairs generally to fascias / soffits / gates	5 days	Wed 01/04/26	Tue 07/04/26
93	External Decorations	5 days	Wed 08/04/26	Tue 14/04/26
94	Internal Decorations	4 days	Tue 31/03/26	Fri 03/04/26
95	Survey flat FED's & report	1 day	Fri 20/02/26	Fri 20/02/26
96	Overhaul communal & FED doors	4 days	Wed 25/03/26	Mon 30/03/26
97	Contar Resin coatings to commun	3 days	Mon 06/04/26	Wed 08/04/26
98	Overhaul / replace electric fans	3 days	Tue 10/03/26	Thu 12/03/26
99	FRA works	2 days	Wed 18/03/26	Thu 19/03/26
100	CCTV to drainage	1 day	Fri 27/03/26	Fri 27/03/26
101	Scaffold Strike	2 days	Wed 15/04/26	Thu 16/04/26
102	**1-11 McDermott Close**	**41 days**	**Mon 23/02/26**	**Mon 20/04/26**
103	Scaffold Erection	3 days	Mon 30/03/26	Wed 01/04/26
104	Asbestos Survey	1 day	Thu 02/04/26	Thu 02/04/26

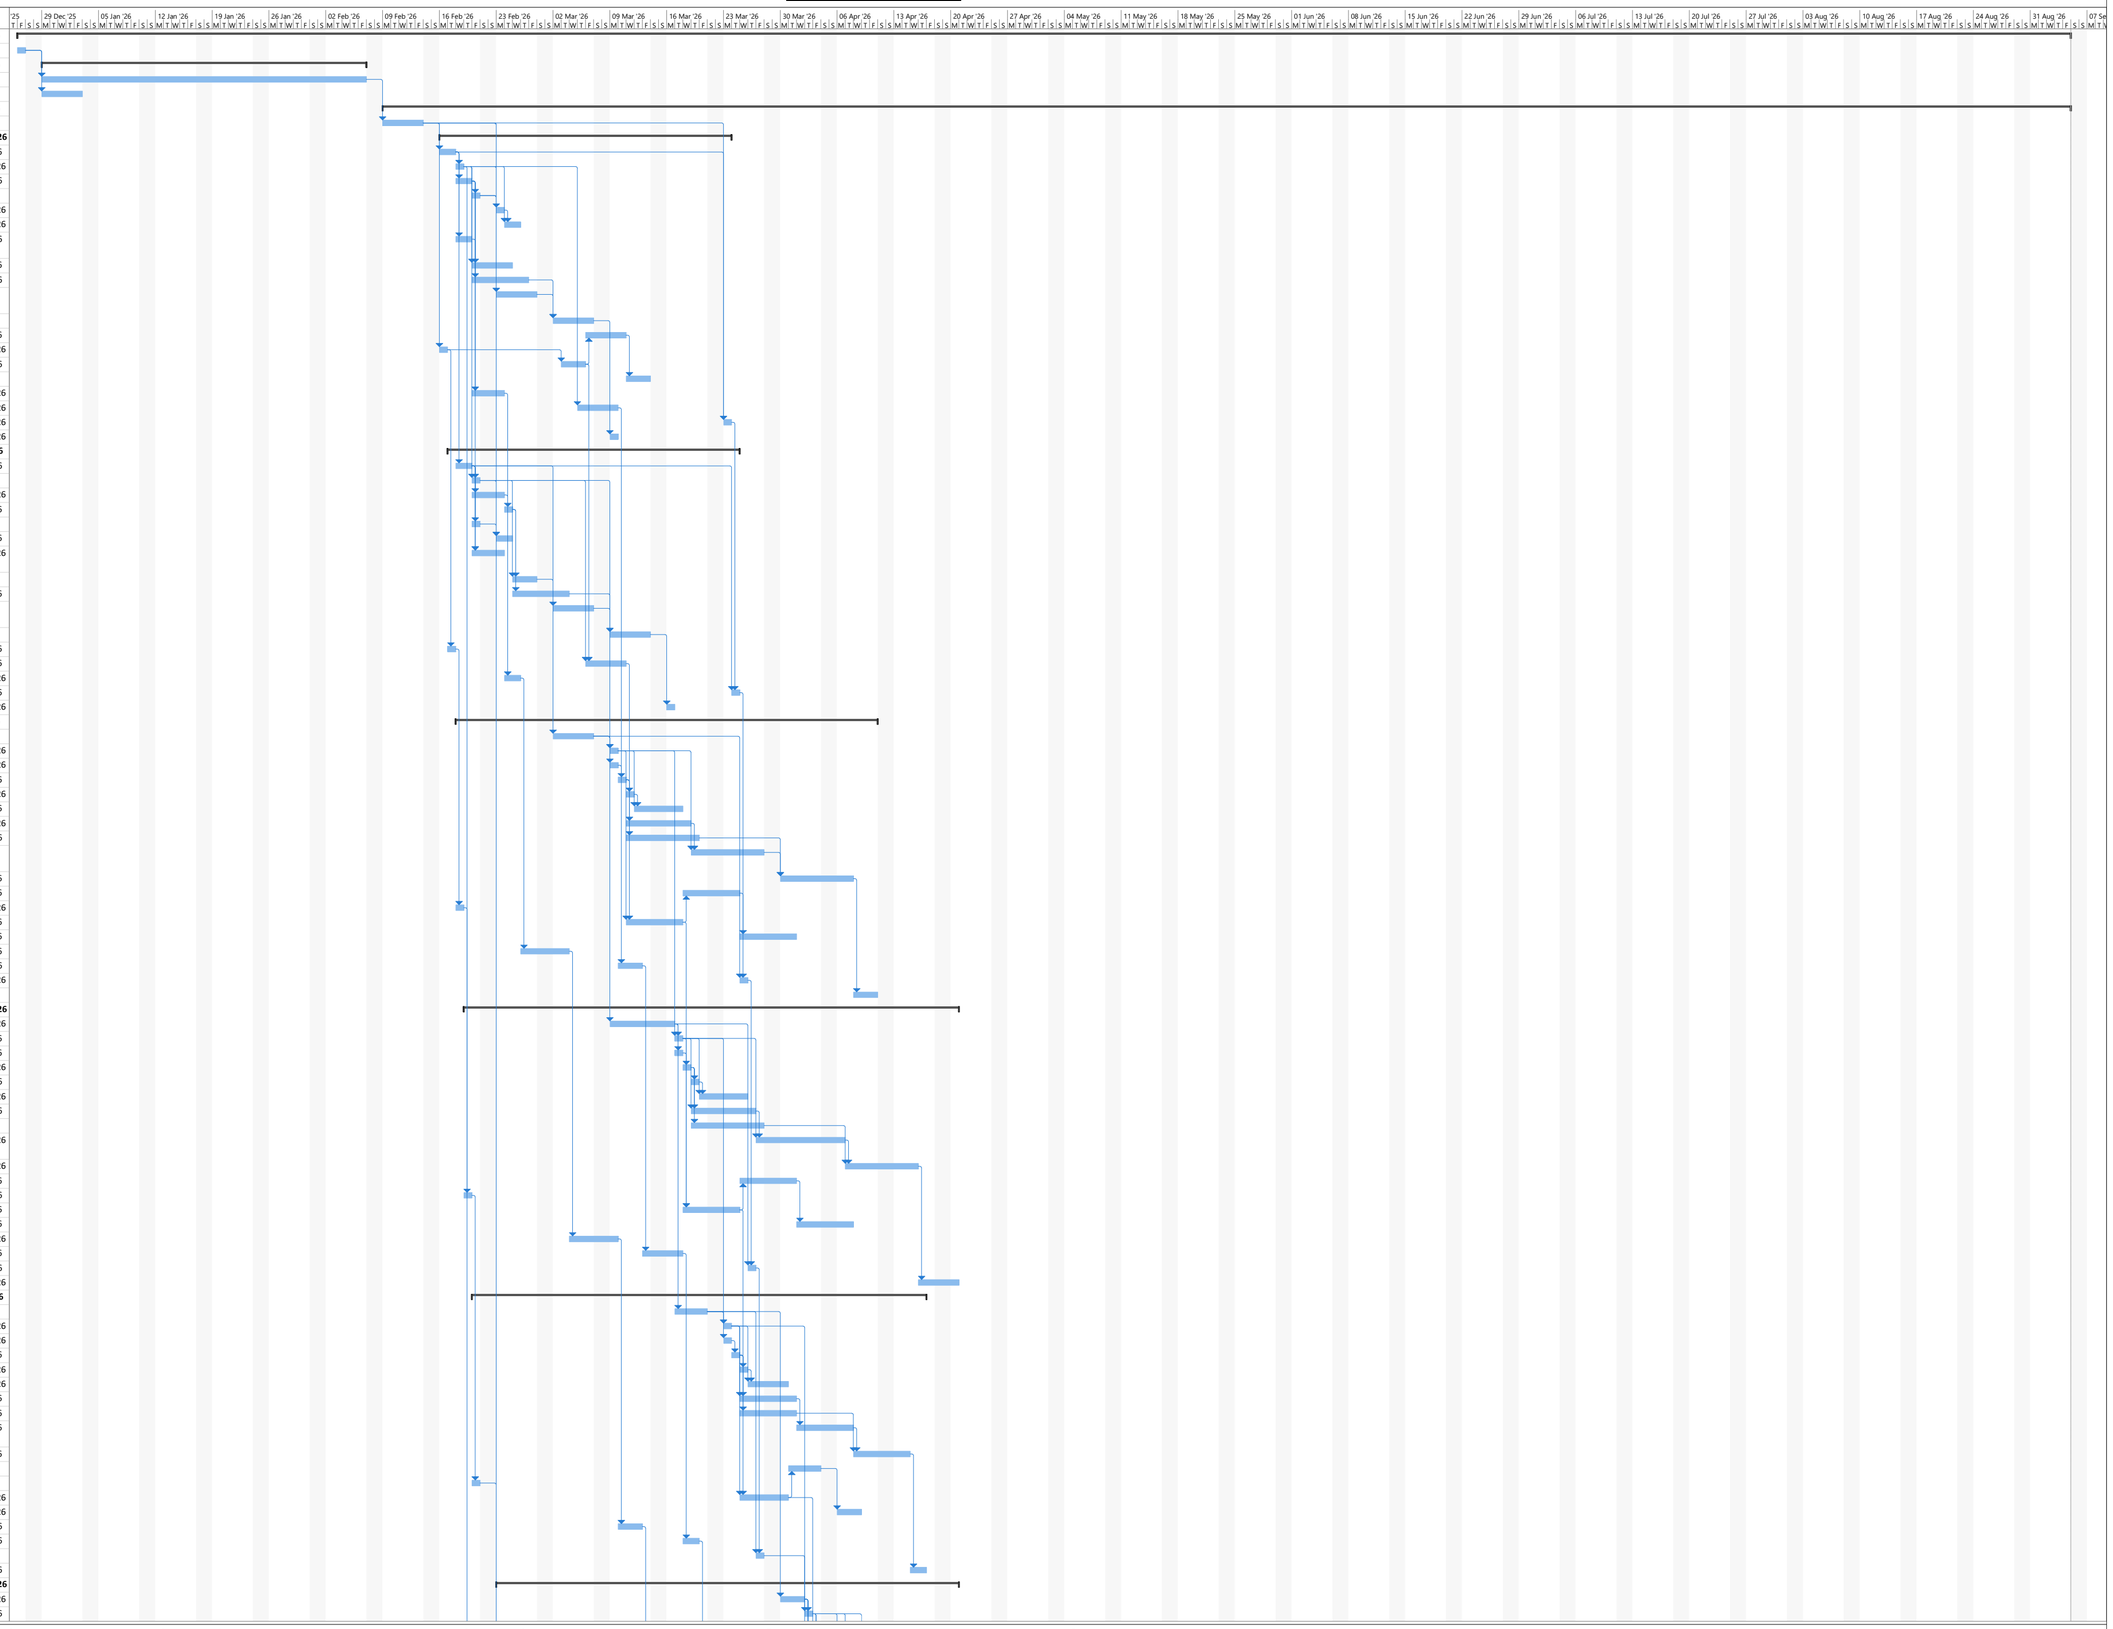

Project: Kambala Estate - Optio
Date: Fri 28/11/25

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

Kambala Estate

ID	Task Name	Duration	Start	Finish
105	Clean masonry	1 day	Thu 02/04/26	Thu 02/04/26
106	Clean through gutters & down pip	1 day	Fri 03/04/26	Fri 03/04/26
107	Roof Inspection & Report	1 day	Mon 06/04/26	Mon 06/04/26
108	Roof repairs	2 days	Tue 07/04/26	Wed 08/04/26
109	Clean & Overhaul windows	5 days	Mon 06/04/26	Fri 10/04/26
110	Masonry Repairs	5 days	Mon 06/04/26	Fri 10/04/26
111	Timber repairs generally to fascias / soffits / gates	5 days	Fri 03/04/26	Thu 09/04/26
112	External Decorations	5 days	Mon 13/04/26	Fri 17/04/26
113	Internal Decorations	4 days	Thu 09/04/26	Tue 14/04/26
114	Survey flat FED's & report	1 day	Mon 23/02/26	Mon 23/02/26
115	Overhaul communal & FED doors	4 days	Fri 03/04/26	Wed 08/04/26
116	Contar Resin coatings to commun	3 days	Wed 15/04/26	Fri 17/04/26
117	Overhaul / replace electric fans	3 days	Fri 13/03/26	Tue 17/03/26
118	FRA works	2 days	Fri 20/03/26	Mon 23/03/26
119	CCTV to drainage	1 day	Thu 02/04/26	Thu 02/04/26
120	Scaffold Strike	1 day	Mon 20/04/26	Mon 20/04/26
121	**13-31 McDermott Close**	**52 days**	**Tue 24/02/26**	**Wed 06/05/26**
122	Scaffold Erection	5 days	Thu 02/04/26	Wed 08/04/26
123	Asbestos Survey	1 day	Thu 09/04/26	Thu 09/04/26
124	Clean masonry	1 day	Thu 09/04/26	Thu 09/04/26
125	Clean through gutters & down pip	1 day	Fri 10/04/26	Fri 10/04/26
126	Roof Inspection & Report	1 day	Mon 13/04/26	Mon 13/04/26
127	Roof repairs	3 days	Tue 14/04/26	Thu 16/04/26
128	Clean & Overhaul windows	5 days	Mon 13/04/26	Fri 17/04/26
129	Masonry Repairs	5 days	Mon 13/04/26	Fri 17/04/26
130	Timber repairs generally to fascias / soffits / gates	5 days	Mon 20/04/26	Fri 24/04/26
131	External Decorations	5 days	Mon 27/04/26	Fri 01/05/26
132	Internal Decorations	4 days	Thu 16/04/26	Tue 21/04/26
133	Survey flat FED's & report	1 day	Tue 24/02/26	Tue 24/02/26
134	Overhaul communal & FED doors	4 days	Fri 10/04/26	Wed 15/04/26
135	Overhaul / replace electric fans	3 days	Wed 18/03/26	Fri 20/03/26
136	CCTV to drainage	1 day	Thu 09/04/26	Thu 09/04/26
137	Scaffold Strike	3 days	Mon 04/05/26	Wed 06/05/26
138	**33-79 McDermott Close**	**70 days**	**Wed 25/02/26**	**Tue 02/06/26**
139	Scaffold Erection	6 days	Mon 20/04/26	Mon 27/04/26
140	Asbestos Survey	1 day	Tue 28/04/26	Tue 28/04/26
141	Clean masonry	1 day	Tue 28/04/26	Tue 28/04/26
142	Clean through gutters & down pip	1 day	Wed 29/04/26	Wed 29/04/26
143	Roof Inspection & Report	1 day	Thu 30/04/26	Thu 30/04/26
144	Roof repairs	4 days	Fri 01/05/26	Wed 06/05/26
145	Liquid Waterproof coating to to rear terrace area	3 days	Tue 28/04/26	Thu 30/04/26
146	Clean & Overhaul windows	7 days	Thu 30/04/26	Fri 08/05/26
147	Masonry Repairs	7 days	Thu 30/04/26	Fri 08/05/26
148	Timber repairs generally to fascias / soffits / gates /bin	7 days	Mon 11/05/26	Tue 19/05/26
149	External Decorations	7 days	Wed 20/05/26	Thu 28/05/26
150	Internal Decorations	7 days	Thu 07/05/26	Fri 15/05/26
151	Survey flat FED's & report	1 day	Wed 25/02/26	Wed 25/02/26
152	Overhaul communal & FED doors	6 days	Wed 29/04/26	Wed 06/05/26
153	Contar Resin coatings to commun	5 days	Mon 18/05/26	Fri 22/05/26
154	Overhaul / replace electric fans	3 days	Mon 23/03/26	Wed 25/03/26
155	FRA works	3 days	Tue 24/03/26	Thu 26/03/26
156	CCTV to drainage	1 day	Tue 28/04/26	Tue 28/04/26
157	Scaffold Strike	3 days	Fri 29/05/26	Tue 02/06/26
158	**2-18 McDermott Close**	**64 days**	**Thu 26/02/26**	**Tue 26/05/26**
159	Scaffold Erection	3 days	Tue 28/04/26	Thu 30/04/26
160	Asbestos Survey	1 day	Fri 01/05/26	Fri 01/05/26
161	Clean masonry	1 day	Fri 01/05/26	Fri 01/05/26
162	Clean through gutters & down pip	1 day	Mon 04/05/26	Mon 04/05/26
163	Roof Inspection & Report	1 day	Tue 05/05/26	Tue 05/05/26
164	Roof repairs	2 days	Wed 06/05/26	Thu 07/05/26
165	Clean & Overhaul windows	5 days	Tue 05/05/26	Mon 11/05/26
166	Masonry Repairs	5 days	Tue 05/05/26	Mon 11/05/26
167	Timber repairs generally to fascias / soffits / gates /bin	5 days	Tue 12/05/26	Mon 18/05/26
168	External Decorations	5 days	Tue 19/05/26	Mon 25/05/26
169	Internal Decorations	5 days	Wed 13/05/26	Tue 19/05/26
170	Survey flat FED's & report	1 day	Thu 26/02/26	Thu 26/02/26
171	Overhaul communal & FED doors	4 days	Thu 07/05/26	Tue 12/05/26
172	Contar Resin coatings to commun	3 days	Wed 20/05/26	Fri 22/05/26
173	Overhaul / replace electric fans	2 days	Thu 26/03/26	Fri 27/03/26
174	FRA works	2 days	Fri 27/03/26	Mon 30/03/26
175	CCTV to drainage	1 day	Fri 01/05/26	Fri 01/05/26
176	Scaffold Strike	1 day	Tue 26/05/26	Tue 26/05/26
177	**20-28 McDermott Close**	**72 days**	**Fri 27/02/26**	**Mon 08/06/26**
178	Scaffold Erection	3 days	Mon 11/05/26	Wed 13/05/26
179	Asbestos Survey	1 day	Thu 14/05/26	Thu 14/05/26
180	Clean masonry	1 day	Thu 14/05/26	Thu 14/05/26
181	Clean through gutters & down pip	1 day	Fri 15/05/26	Fri 15/05/26
182	Roof Inspection & Report	1 day	Mon 18/05/26	Mon 18/05/26
183	Roof repairs	2 days	Tue 19/05/26	Wed 20/05/26
184	Clean & Overhaul windows	5 days	Mon 18/05/26	Fri 22/05/26
185	Masonry Repairs	5 days	Mon 18/05/26	Fri 22/05/26
186	Timber repairs generally to fascias / soffits / gates	5 days	Mon 25/05/26	Fri 29/05/26
187	External Decorations	5 days	Mon 01/06/26	Fri 05/06/26
188	Internal Decorations	5 days	Thu 21/05/26	Wed 27/05/26
189	Survey flat FED's & report	1 day	Fri 27/02/26	Fri 27/02/26
190	Overhaul communal & FED doors	4 days	Fri 15/05/26	Wed 20/05/26
191	Overhaul / replace electric fans	2 days	Mon 30/03/26	Tue 31/03/26
192	FRA works	2 days	Tue 31/03/26	Wed 01/04/26
193	CCTV to drainage	1 day	Thu 14/05/26	Thu 14/05/26
194	Scaffold Strike	1 day	Mon 08/06/26	Mon 08/06/26
195	**30-94 McDermott Close**	**86 days**	**Mon 02/03/26**	**Mon 29/06/26**
196	Scaffold Erection	7 days	Thu 14/05/26	Fri 22/05/26
197	Asbestos Survey	1 day	Mon 25/05/26	Mon 25/05/26
198	Clean masonry	1 day	Mon 25/05/26	Mon 25/05/26
199	Clean through gutters & down pip	1 day	Tue 26/05/26	Tue 26/05/26
200	Roof Inspection & Report	1 day	Wed 27/05/26	Wed 27/05/26
201	Roof repairs	4 days	Thu 28/05/26	Tue 02/06/26
202	Liquid Waterproof coating to to rear terrace area	3 days	Mon 25/05/26	Wed 27/05/26
203	Clean & Overhaul windows	7 days	Wed 27/05/26	Thu 04/06/26
204	Masonry Repairs	7 days	Wed 27/05/26	Thu 04/06/26
205	Timber repairs generally to fascias / soffits / gates /bin	7 days	Fri 05/06/26	Mon 15/06/26
206	External Decorations	7 days	Tue 16/06/26	Wed 24/06/26
207	Internal Decorations	7 days	Wed 03/06/26	Thu 11/06/26

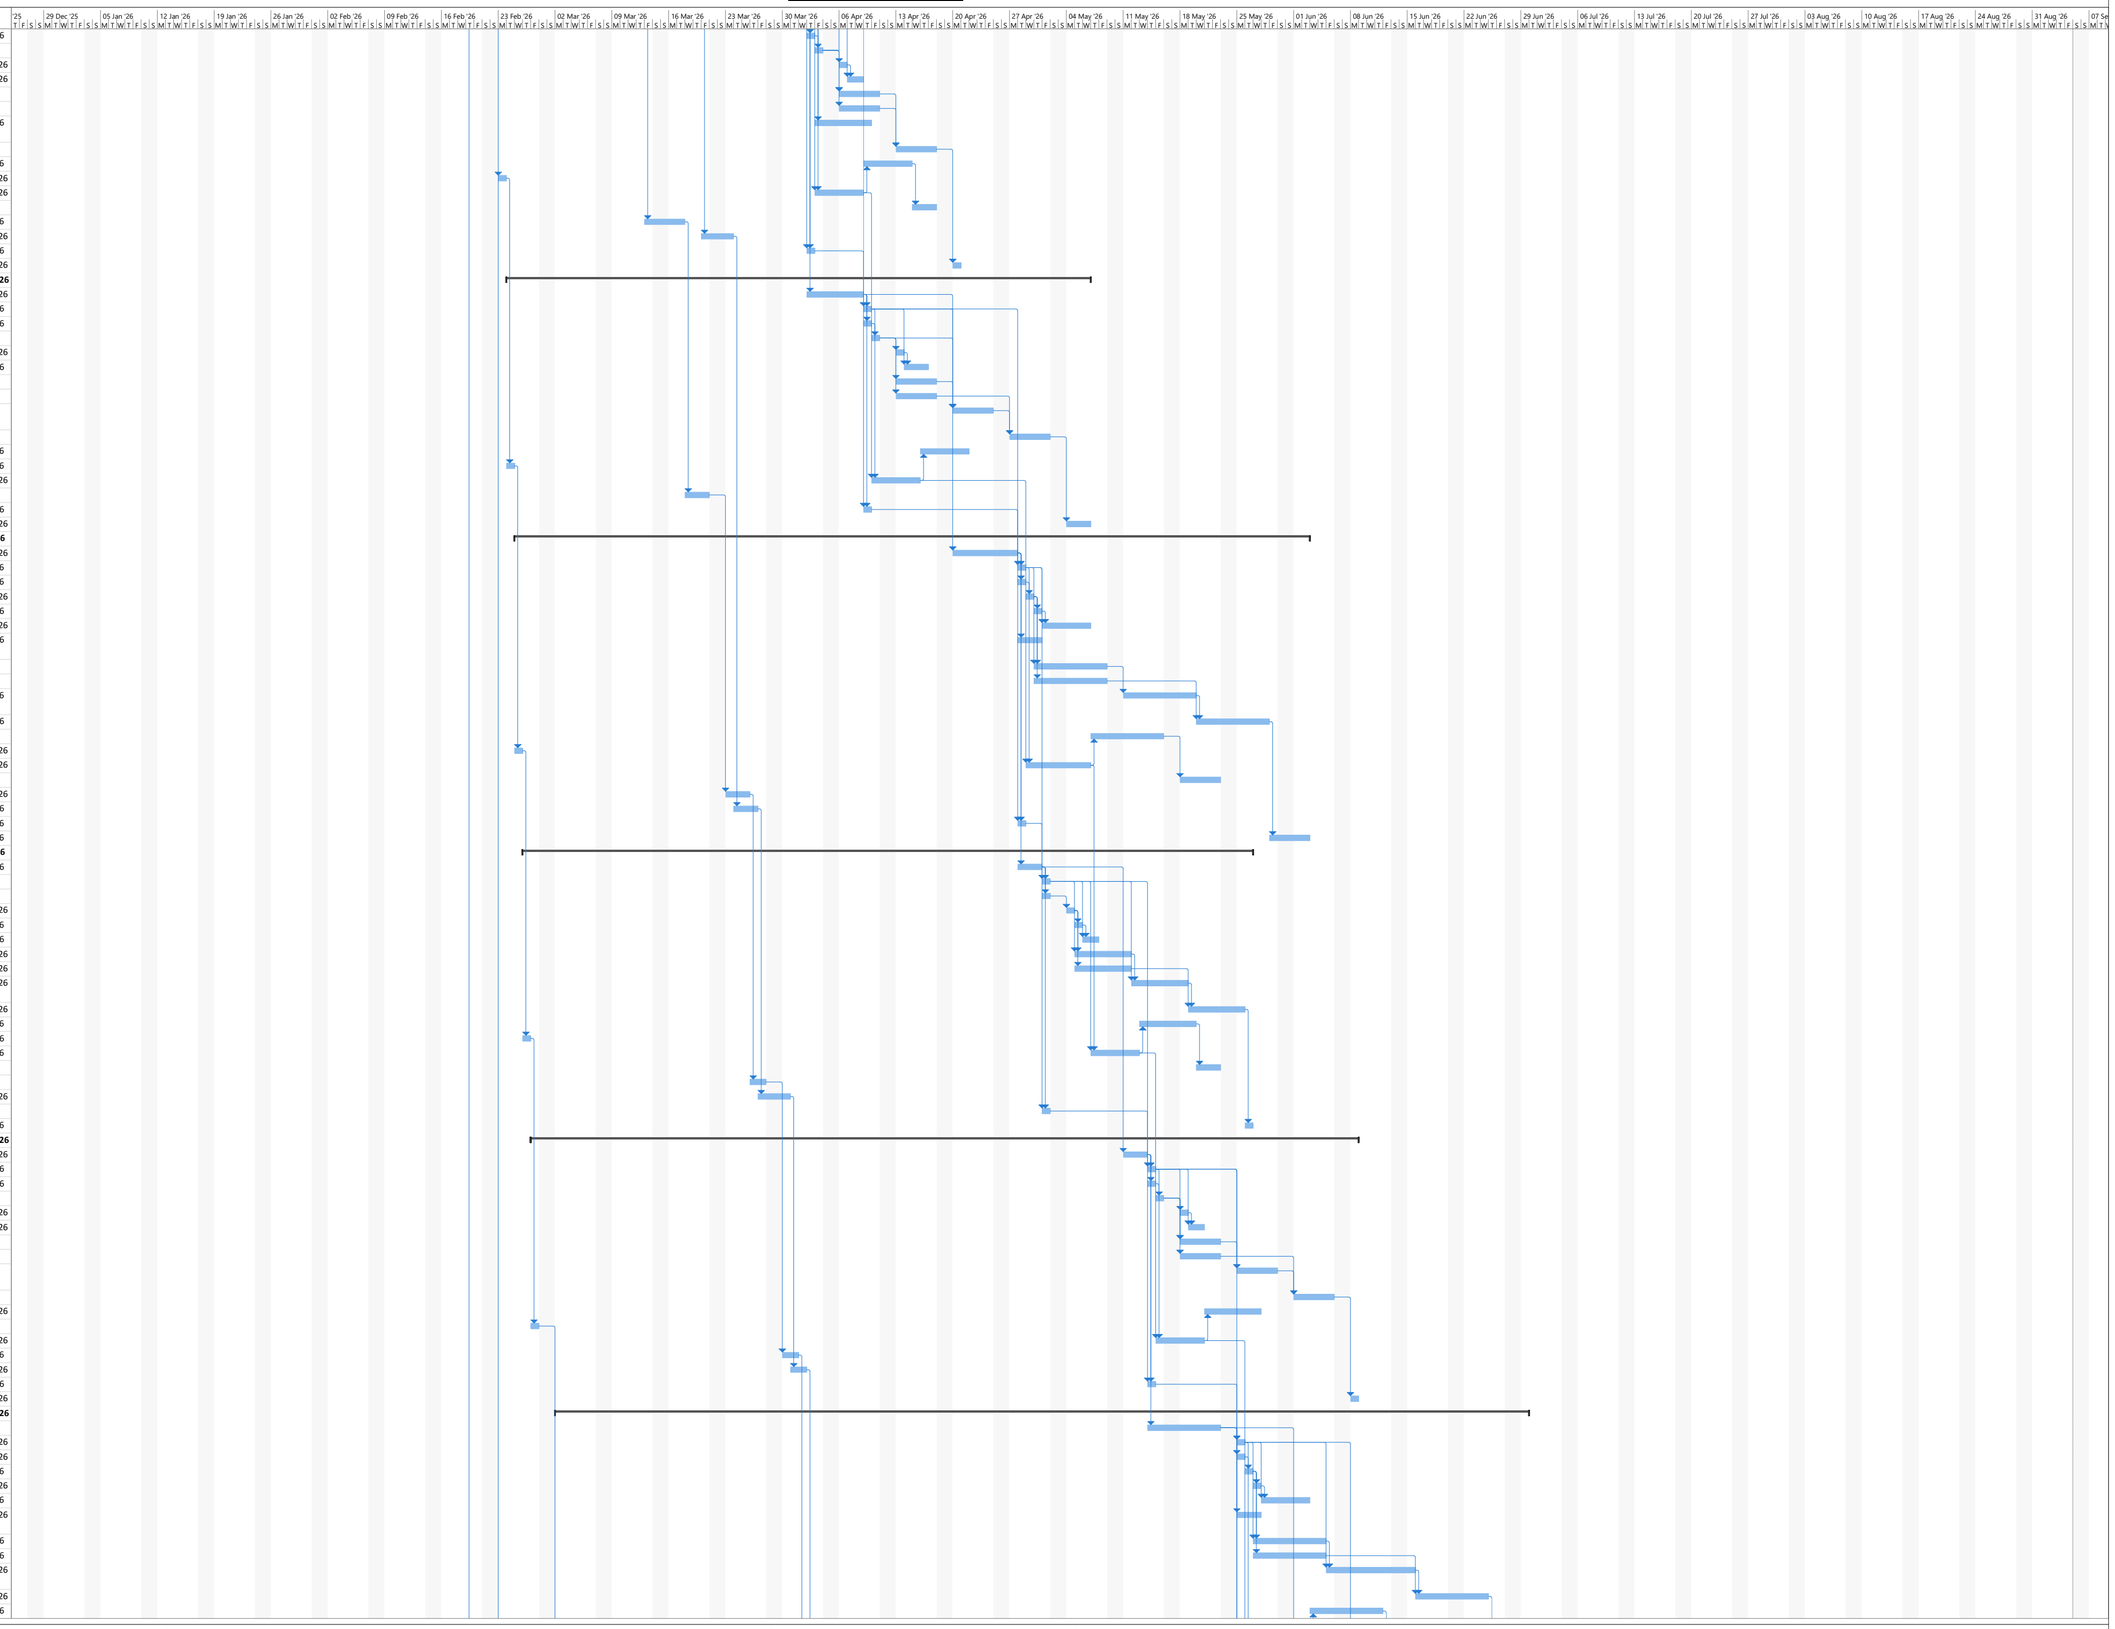

Project: Kambala Estate - Optio
Date: Fri 28/11/25

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

Kambala Estate

ID	Task Name	Duration	Start	Finish
208	Survey flat FED's & report	1 day	Mon 02/03/26	Mon 02/03/26
209	Overhaul communal & FED doors	6 days	Tue 26/05/26	Tue 02/06/26
210	Contar Resin coatings to commun	8 days	Fri 12/06/26	Tue 23/06/26
211	Overhaul / replace electric fans	3 days	Wed 01/04/26	Fri 03/04/26
212	FRA works	3 days	Thu 02/04/26	Mon 06/04/26
213	CCTV to drainage	1 day	Mon 25/05/26	Mon 25/05/26
214	Scaffold Strike	3 days	Thu 25/06/26	Mon 29/06/26
215	**1-29 Wolfencroft Close**	**91 days**	**Tue 03/03/26**	**Tue 07/07/26**
216	Scaffold Erection	5 days	Mon 01/06/26	Fri 05/06/26
217	Asbestos Survey	1 day	Mon 08/06/26	Mon 08/06/26
218	Clean masonry	1 day	Mon 08/06/26	Mon 08/06/26
219	Clean through gutters & down pip	1 day	Tue 09/06/26	Tue 09/06/26
220	Roof Inspection & Report	1 day	Wed 10/06/26	Wed 10/06/26
221	Roof repairs	2 days	Thu 11/06/26	Fri 12/06/26
222	Liquid Waterproof coating to to rear terrace area	3 days	Mon 08/06/26	Wed 10/06/26
223	Clean & Overhaul windows	5 days	Thu 11/06/26	Wed 17/06/26
224	Masonry Repairs	5 days	Wed 10/06/26	Tue 16/06/26
225	Timber repairs generally to fascias / soffits / gates /bin	5 days	Thu 18/06/26	Wed 24/06/26
226	External Decorations	6 days	Thu 25/06/26	Thu 02/07/26
227	Internal Decorations	6 days	Tue 16/06/26	Tue 23/06/26
228	Survey flat FED's & report	1 day	Tue 03/03/26	Tue 03/03/26
229	Overhaul communal & FED doors	5 days	Tue 09/06/26	Mon 15/06/26
230	Contar Resin coatings to commun	6 days	Wed 24/06/26	Wed 01/07/26
231	Overhaul / replace electric fans	3 days	Mon 06/04/26	Wed 08/04/26
232	FRA works	3 days	Tue 07/04/26	Thu 09/04/26
233	CCTV to drainage	1 day	Mon 08/06/26	Mon 08/06/26
234	Scaffold Strike	3 days	Fri 03/07/26	Tue 07/07/26
235	**31-61 Wolfencroft Close**	**95 days**	**Wed 04/03/26**	**Tue 14/07/26**
236	Scaffold Erection	6 days	Mon 08/06/26	Mon 15/06/26
237	Asbestos Survey	1 day	Tue 16/06/26	Tue 16/06/26
238	Clean masonry	1 day	Tue 16/06/26	Tue 16/06/26
239	Clean through gutters & down pip	1 day	Wed 17/06/26	Wed 17/06/26
240	Roof Inspection & Report	1 day	Thu 18/06/26	Thu 18/06/26
241	Roof repairs	3 days	Fri 19/06/26	Tue 23/06/26
242	Clean & Overhaul windows	5 days	Thu 18/06/26	Wed 24/06/26
243	Masonry Repairs	5 days	Thu 18/06/26	Wed 24/06/26
244	Timber repairs generally to fascias / soffits / gates	5 days	Thu 25/06/26	Wed 01/07/26
245	External Decorations	6 days	Thu 02/07/26	Thu 09/07/26
246	Survey flat FED's & report	1 day	Wed 04/03/26	Wed 04/03/26
247	Overhaul FED doors	5 days	Wed 17/06/26	Tue 23/06/26
248	Overhaul / replace electric fans	3 days	Thu 09/04/26	Mon 13/04/26
249	CCTV to drainage	1 day	Tue 16/06/26	Tue 16/06/26
250	Scaffold Strike	3 days	Fri 10/07/26	Tue 14/07/26
251	**4-8 Wolfencroft Close**	**98 days**	**Thu 05/03/26**	**Mon 20/07/26**
252	Scaffold Erection	3 days	Mon 29/06/26	Wed 01/07/26
253	Asbestos Survey	1 day	Thu 02/07/26	Thu 02/07/26
254	Clean masonry	1 day	Thu 02/07/26	Thu 02/07/26
255	Clean through gutters & down pip	1 day	Fri 03/07/26	Fri 03/07/26
256	Roof Inspection & Report	1 day	Mon 06/07/26	Mon 06/07/26
257	Roof repairs	2 days	Tue 07/07/26	Wed 08/07/26
258	Clean & Overhaul windows	3 days	Mon 06/07/26	Wed 08/07/26
259	Masonry Repairs	3 days	Mon 06/07/26	Wed 08/07/26
260	Timber repairs generally to fascias / soffits / gates	3 days	Thu 09/07/26	Mon 13/07/26
261	External Decorations	4 days	Tue 14/07/26	Fri 17/07/26
262	Survey flat FED's & report	1 day	Thu 05/03/26	Thu 05/03/26
263	Overhaul FED doors	5 days	Fri 03/07/26	Thu 09/07/26
264	Overhaul / replace electric fans	3 days	Tue 14/04/26	Thu 16/04/26
265	CCTV to drainage	1 day	Thu 02/07/26	Thu 02/07/26
266	Scaffold Strike	1 day	Mon 20/07/26	Mon 20/07/26
267	**10-26 Wolfencroft Close**	**105 days**	**Fri 06/03/26**	**Thu 30/07/26**
268	Scaffold Erection	3 days	Thu 02/07/26	Mon 06/07/26
269	Asbestos Survey	1 day	Tue 07/07/26	Tue 07/07/26
270	Clean masonry	1 day	Tue 07/07/26	Tue 07/07/26
271	Clean through gutters & down pip	1 day	Wed 08/07/26	Wed 08/07/26
272	Roof Inspection & Report	1 day	Thu 09/07/26	Thu 09/07/26
273	Roof repairs	2 days	Fri 10/07/26	Mon 13/07/26
274	Liquid Waterproof coating to to rear terrace area	3 days	Tue 07/07/26	Thu 09/07/26
275	Clean & Overhaul windows	5 days	Thu 09/07/26	Wed 15/07/26
276	Masonry Repairs	5 days	Thu 09/07/26	Wed 15/07/26
277	Timber repairs generally to fascias / soffits / gates /bin	5 days	Thu 16/07/26	Wed 22/07/26
278	External Decorations	5 days	Thu 23/07/26	Wed 29/07/26
279	Internal Decorations	5 days	Thu 16/07/26	Wed 22/07/26
280	Survey flat FED's & report	1 day	Fri 06/03/26	Fri 06/03/26
281	Overhaul communal & FED doors	4 days	Fri 10/07/26	Wed 15/07/26
282	Contar Resin coatings to communal floor	4 days	Thu 23/07/26	Tue 28/07/26
283	Overhaul / replace electric fans	2 days	Fri 17/04/26	Mon 20/04/26
284	FRA works	2 days	Fri 10/04/26	Mon 13/04/26
285	CCTV to drainage	1 day	Tue 07/07/26	Tue 07/07/26
286	Scaffold Strike	1 day	Thu 30/07/26	Thu 30/07/26
287	**Haven Lodge**	**142 days**	**Thu 19/02/26**	**Fri 04/09/26**
288	Scaffold Erection	7 days	Tue 07/07/26	Wed 15/07/26
289	Asbestos Survey	1 day	Thu 19/02/26	Thu 19/02/26
290	Clean masonry	2 days	Thu 16/07/26	Fri 17/07/26
291	Clean through gutters & down pip	1 day	Mon 20/07/26	Mon 20/07/26
292	Roof Inspection & Report	1 day	Tue 21/07/26	Tue 21/07/26
293	Roof repairs	5 days	Wed 22/07/26	Tue 28/07/26
294	Clean & Overhaul windows	20 days	Tue 21/07/26	Mon 17/08/26
295	Masonry Repairs	10 days	Tue 21/07/26	Mon 03/08/26
296	Timber repairs generally to fascias / soffits / gates /bin	5 days	Tue 18/08/26	Mon 24/08/26
297	External Decorations	5 days	Tue 25/08/26	Mon 31/08/26
298	Internal Decorations	30 days	Mon 13/04/26	Fri 22/05/26
299	Survey flat FED's & report	5 days	Mon 23/02/26	Fri 27/02/26
300	Overhaul communal & FED doors	20 days	Mon 16/03/26	Fri 10/04/26
301	New Vinyl Flooring	30 days	Mon 25/05/26	Fri 03/07/26
302	Overhaul / replace electric fans	10 days	Mon 23/02/26	Fri 06/03/26
303	FRA works to loft space	50 days	Mon 23/02/26	Fri 01/05/26
304	Overhaul to sanitaryware	5 days	Mon 23/03/26	Fri 27/03/26
305	Renewal of 1Nr Kitchen	6 days	Mon 23/03/26	Mon 30/03/26
306	CCTV to drainage	1 day	Thu 16/07/26	Thu 16/07/26
307	Scaffold Strike	4 days	Tue 01/09/26	Fri 04/09/26

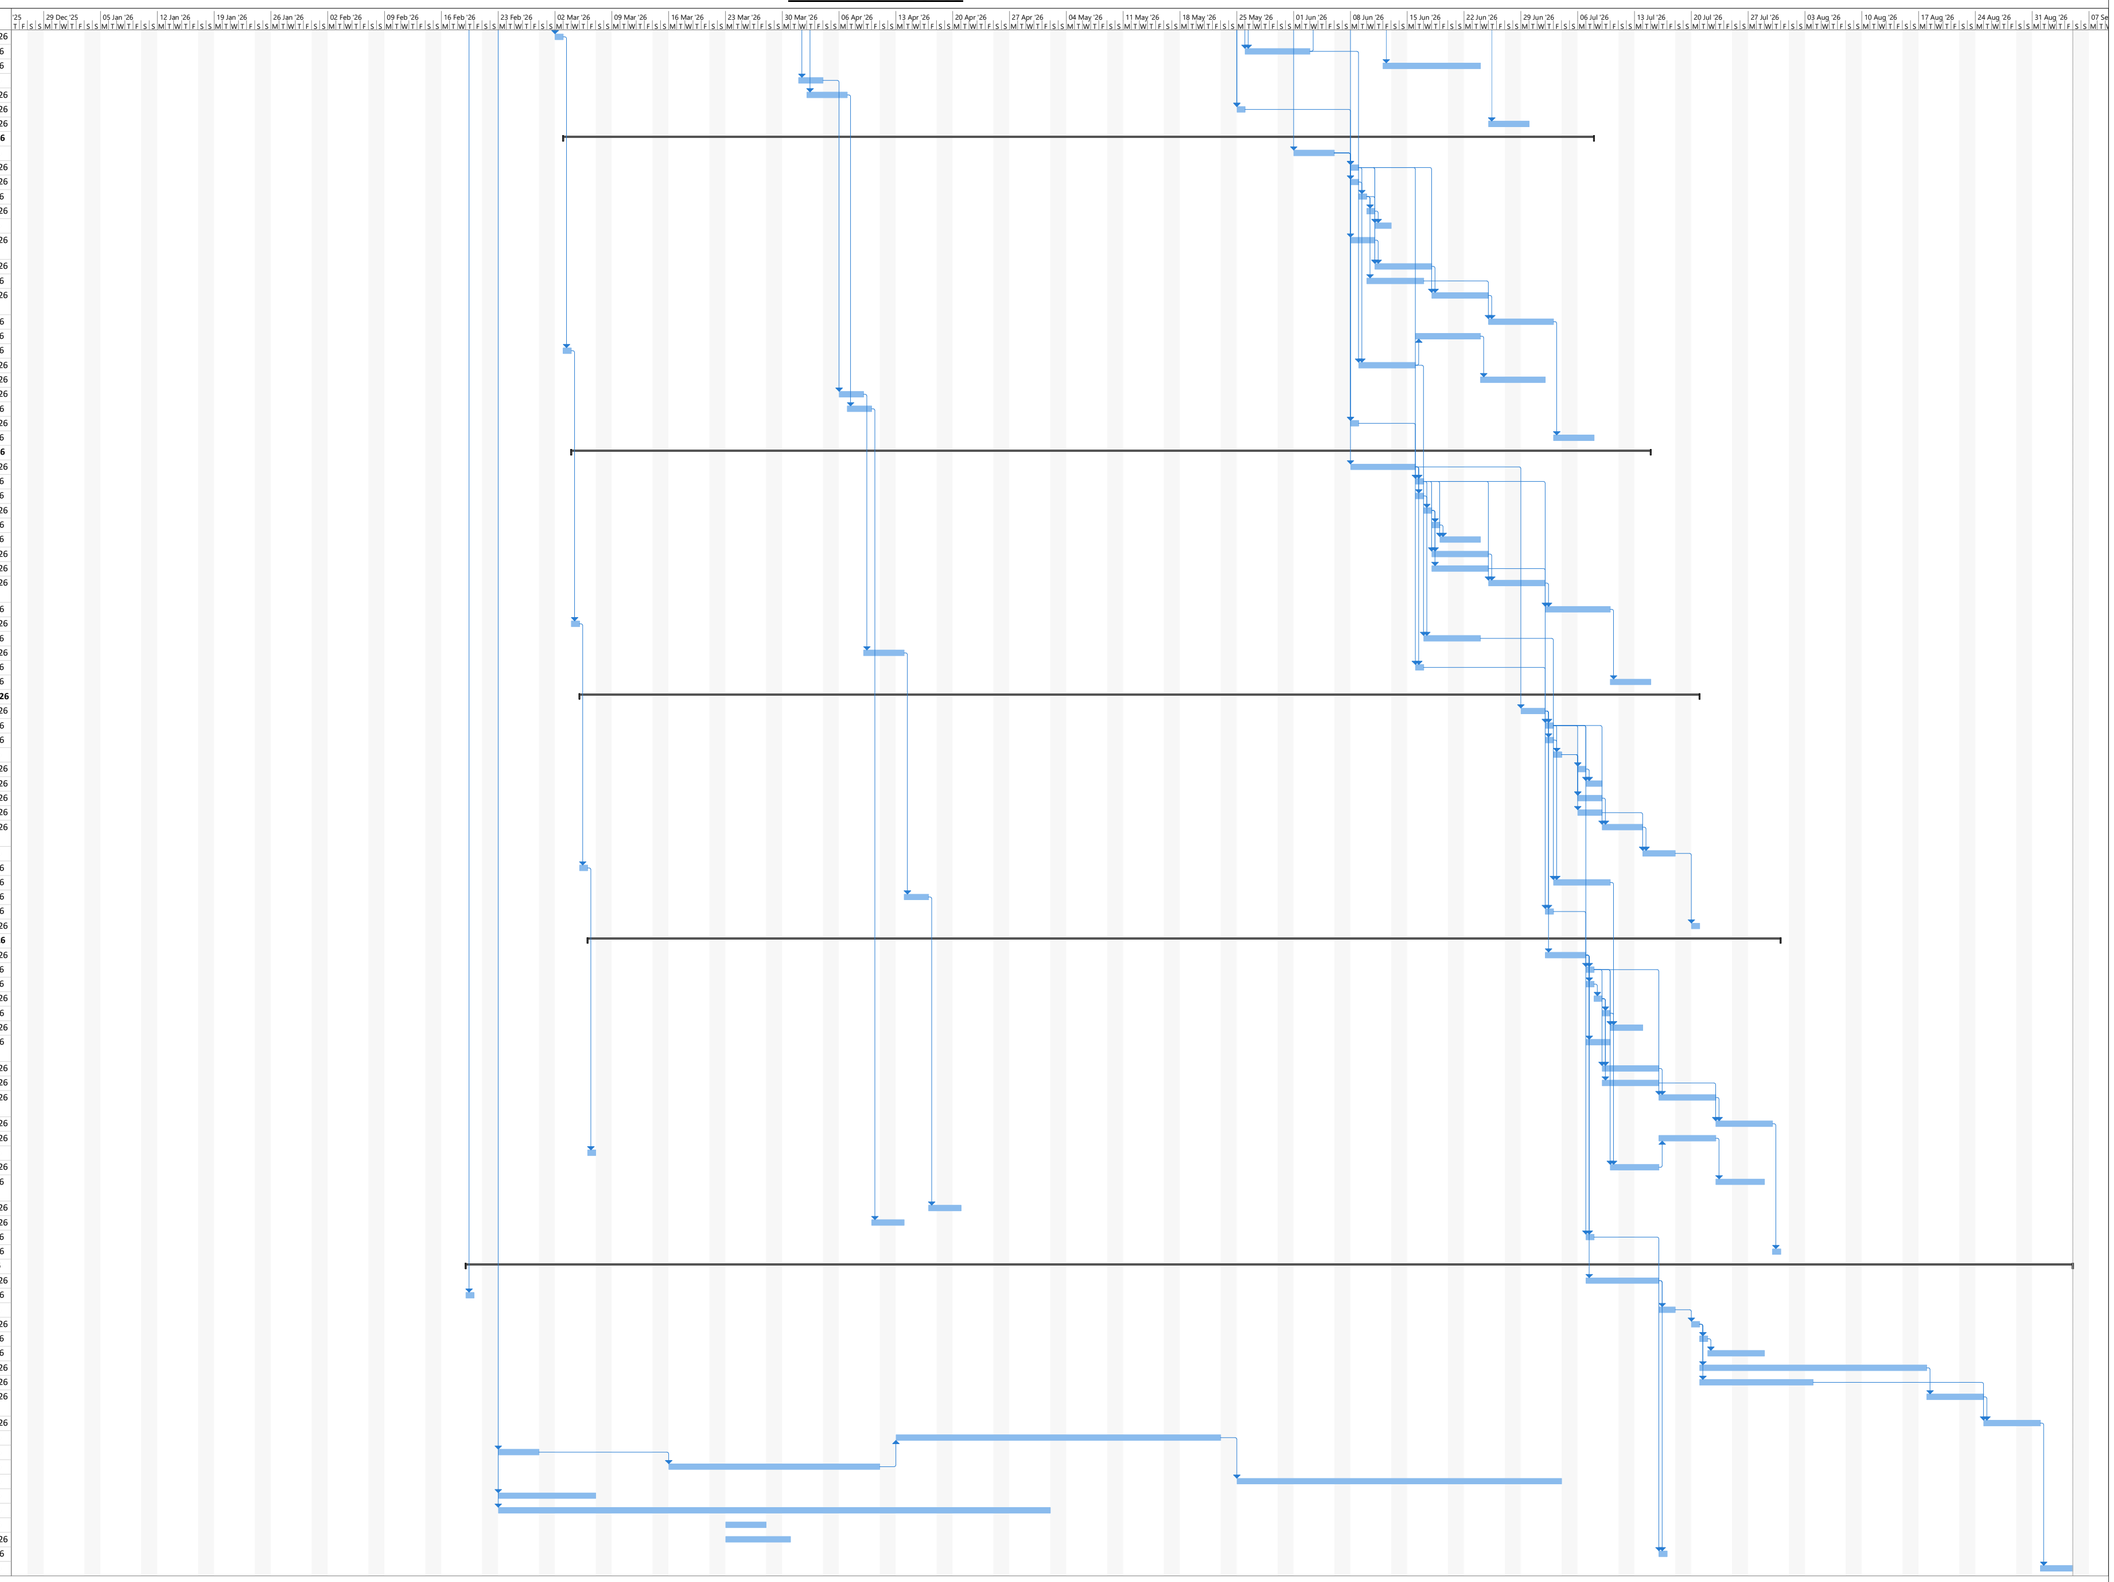

Project: Kambala Estate - Optio
Date: Fri 28/11/25

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
